



West 28th Street Substation Project

Construction Look Ahead for the week of September 25, 2023

Helpful Links

[Project Website](#)



Project Website

[Project Details](#)

[West 28 St Substation FAQ](#)

[VIDEO: Core Infrastructure - Substations](#)

[VIDEO: What is CBTC?](#)

[About CBTC upgrades](#)

[Other MTA Projects](#)

[MTA.info](#)



You are receiving this notice as part of the MTA’s continuing effort to keep the community apprised of construction activities in support of the West 28th Street Substation project.

The MTA’s contractor for the W28th Street Substation Project, Skanska E-J Electric 28S Joint Venture, completed the following items this week:

Main work zone –

- Completed drilling and removed second and final drill rig off site
- Continued excavation of west side of substation and began installing first level of bracing

East work zone –

- Continued excavation for NYC Transit duct bank and manhole.


Work during the week of September 25th, will include, but not be limited to:

- Project Wide – Restriping of 28th Street & Southern 8th Avenue crosswalk.
- Main work zone – Continue excavation for installation of first level of decking.

East work zone –

- Con Edison to splice new cables in preparation for removal of old cables.
- Construct structure for subway roof penetration.
- Continue NYC Transit duct bank and manhole construction.

Stage 2 - Installing/Rerouting Utility Lines, Secant Piles

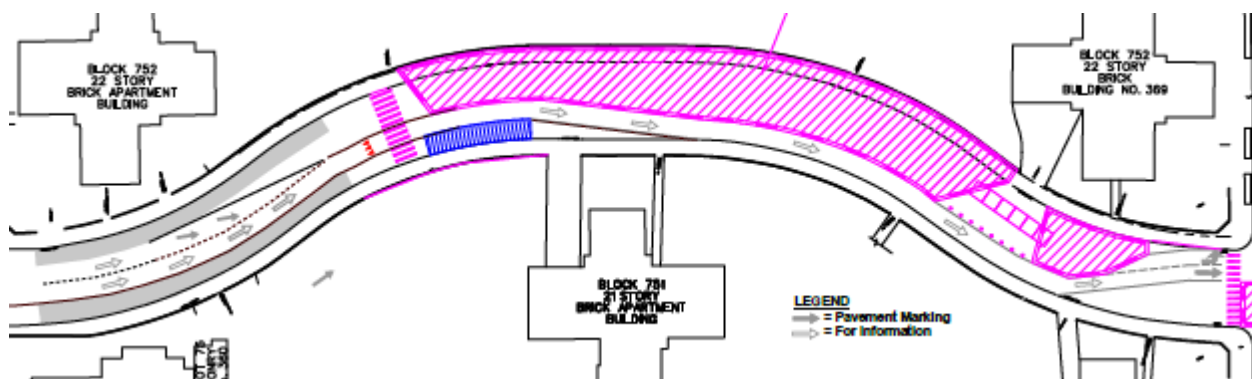


Project Status

Contract Awarded: 10/24/2022

- Contractor: Skanska E-J Electric 28S Joint Venture
- Mobilization: 1/16/2023
- Milestone #1 (restoration of 28 Street): 12/25/2024
- Milestone #2 (Substantial Completion): 9/16/2025
- Final Completion: 12/15/2025

Work hours for the project are 7am to 6pm Monday to Friday, though we anticipate confining the noisiest of work to 8am-4pm.

The contractor is allowed per DOT permit to work 8am-4pm on weekends, but no noisy work is allowed.

The MTA is building a new underground power substation at West 28 Street. This will provide dependable and redundant power for the existing system serving the  subway lines, while also supporting our upgrade to a new train control system which will bring you better, more frequent, and more reliable service.

The community can expect regular communication, throughout the project, including regular construction updates and at key milestones on the [project's webpage](#) and a dedicated email address (w28thoutreach@mtacd.org) to field concerns.

Thank you for your patience while we build this vital public works project.

